PROJEKT MANAGEMENT AUSTRIA
member of IPMA

Project handbook
Wetterstation
001

Version 8
Project manager: Brückl Matthias
Date: 24.11.2025

Content

1 Project plans....5
1.1 Project Assignment....5
1.2 Project Objectives (objectives, non-objectives)....6
1.3 Description of Pre- and Post Project Phase....7
1.4 Project Environment Analysis....8
1.5 Relationship to Other Projects and the Organisations´s Strategy....9
1.6 Project Organisation Chart....10
1.7 Plan of Objects of Consideration of the Project....11
1.8 Work Breakdown Structure (WBS)....12
1.9 Project Work-Package Specification....13
1.10 Project Responsibility Matrix....16
1.11 Milestoneplan....17
1.12 Project Bar Chart....18
1.13 Resource Plan....19
1.14 Project Cost Plan....20
1.15 Project Communication....21
1.16 Project „Rules“....22
1.17 Project Risk Analysis....23
1.18 Project Documentation....24

2 Project Start....25
2.1 Minutes– Project Start....25

3 Project Co-ordination....26
3.1 Approval of Work-packages....26
3.2 Minutes – Project Co-ordination....26

4 Project Controlling....27
4.1 Project Status Report....27
4.2 Additional Project Status Reports....28
4.3 Minutes – Project controlling....28

5 Project Close Down....29
5.1 Project Close Down Report....29
5.2 Minutes – Project Close Down....30

Document versions

Versionno.	Date	Change	Author
1	24.11.25	Start	Brückl M.
2	28.11.25	Objectives and project organization completed	Aistleitner D.
3	29.11.25	Completion till 1.5	Bergbauer K.
4	30.11.25	Completion till 1.9	Bergbauer K. / Aistleitner D.
5	01.12.25	1.4 & 1.9	Aistleitner D.
6	02.12.25	Finishing the Parts for Project Handbook Part 1 up to 1.10	Brückl M.
7	24.01.26	Optimizing project environment graphic	Bergbauer K.
8	25.01.26	Update according the feedback	Brückl M.
9	01.02.26	Update according the feedback and complete 1.13 to 2	Brückl M.
10	02.02.26	First Weekly Report	Bergbauer K.
11	16.02	Weekly Report + Update according the feedback	Brückl M.

Distribution list

Name	Organisational Unit	Role in project	Telephone	E-mail
Brückl Matthias	Project Manager	Backend developer	O664 994484299	Matthias.brueckl@htl-wels.at
Aistleitner Daniel	Project Team Member	Frontend developer	0677 641591985	Daniel.aistleitner@htl-wels.at
Bergbauer Klaus	Project Team Member	Hardware and 3d Modelling	0660 90940434	Klaus.bergbauer@htl-wels.at
HTL-Wels	Project Owner		0664123456789	office@htl-wels.at
Smart Flowerpot	Stakeholder	Help with optimizing	0681 108468979	Paul.auer@htl-wels.at
Smart Wand	Stakeholder	Help with optimizing	0677 632238199	Thomas.toferer@htl-wels.at

1 Project plans

1.1 Project Assignment

Wetterstation 001	PROJECT-ASSIGNMENT
Project start event: • Submission of the Project shandbook	**Project start date:** • 12.01.2026
project close down event in terms of content: • Active usage of the weatherstation **Formal project close down event:** • Handing the weatherstation over to the teacher	**Project close down dates:** • 10.06.2026
Project objectives: • Functioning weather station • Energy-independent power supply • Web based data analyse • Minimalist Case	**Non-objectives:** • No complex data processing • No guarantee of absolute accuracy of the measurement data. • No use of cloud storage (e.g., Google Drive, AWS, Azure). • No failover protection through redundant hardware components. No remote control
Main tasks (Project phases): • Conding Frontend • Read out the date of the sensors • Coding a small database • Coding APIs • 3d modelling the Case	**Project resources and costs*:** resource/type of cost | unit | Costs (€) Raspberry Pi 2w / A | 1 | 30€ BME280 / A | 1 | 5€ DHT22 / A | 1 | 8€ VEML6075 / A | 1 | 10€ Breadboard / A | 1 | 5€ PETG-Filament / A | 3 | 45€
Project owner: • HTL Wels	**Project manager:** • Brückl Matthias
Project team members: • Aistleitner Daniel • Bergbauer Klaus	
..... <*HTL-Wels*>, (Project owner)	..... *<Matthias Brückl>* (Project manager)

* Possible categories of total Project budget:

Category A: up to 0,3 million Euro
Category B: up to 1 million Euro
Category C: up to 10 million Euro
Category D: more than 10 million Euro

1.2 Project Objectives (objectives, non-objectives)

Wetterstation 001	PROJECT OBJECTIVES	
Type of objective	**Project objectives**	**Adjusted project objectives as of...**

objectives:
• **Main objectives**
 	
• **Additional objectives**
	• Readout following sensors:
	  • UV sensor
	  • Temperature sensor
	  • Air pressure sensor
	  • Humidity sensor
	• Energy-independent power supply (24 hours 7 days per week)
	• Web based data analyse
	• Minimalist Case
	
	• Implement a pinwheel to measure wind speed
		•

Non-objectives	• No complex data processing • No guarantee of absolute accuracy of the measurement data. • No use of cloud storage (e.g., Google Drive, AWS, Azure). • No failover protection through redundant hardware components. • No remote control	• If there is enough time left before end of mai this objective could be transformed into an additional object.

1.3 Description of Pre- and Post Project Phase

Wetterstation 001	DESCRIPTION OF PRE- AND POST-PROJECT PHASE

1) Pre-project phase

What triggered the project?

- An assignment for ITP in school
- The idea of the project was given to us by Brückl's mom
- She wants to know the exact temperature in her garden

Relevant documents for the project

- Weatherstation_Goals.docx
- Materiallist.docx
- Wetterstation_Pflichtenheft.docx
- Protokoll.docx

Experience from similar projects

- Groupwork SEW in second class (Aistleitner/Brückl/Bergbauer)
- Built a react Website (Brückl)
-

2) Post-project phase

- Project will be presented on the "Open House Day" at School

1.4 Project Environment Analysis

Wetterstation 001

PROJECT ENVIRONMENT GRAPHIC

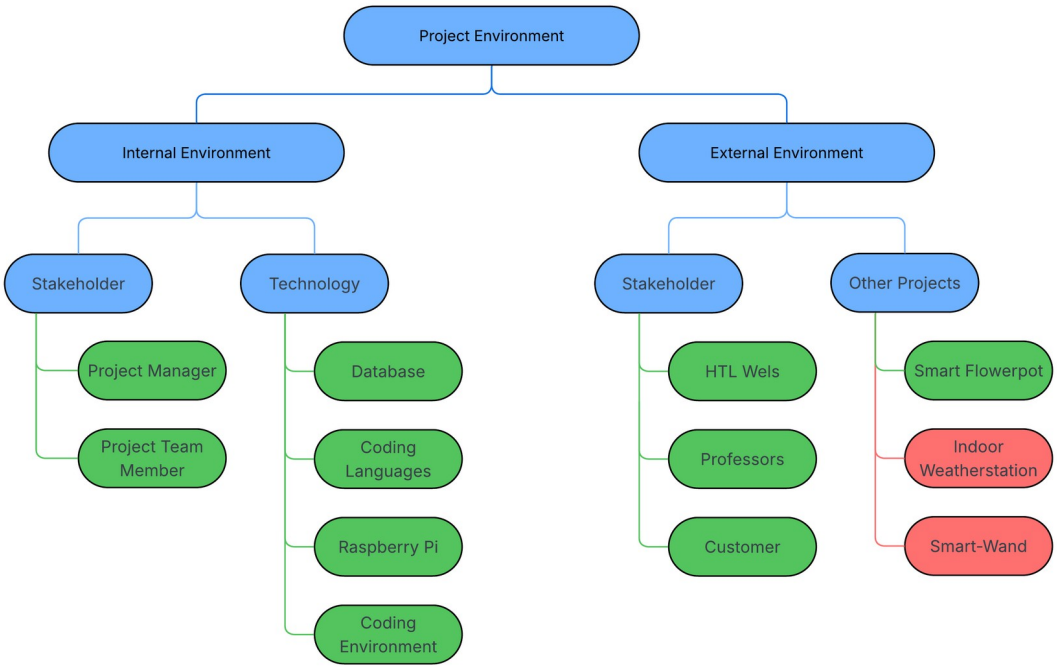

Wetterstation 001

PROJECT ENVIRONMENT TABLE

Environment	**Relationship** (potential/conflict)	**Measures**	**Who / when** **PSP Code**
Stakeholder	potential	Can help us to optimize our project	HTL-Wels/ Professors
Other Projects	conflict	Are competition	Indoor Wetterstation
Other Projects	potential	can help each other	Smart-Flowerpot/ Smart-Wand
Technology	potential	help us to implement it as we envision it	Database/Coding languages/ Raspberry Pi

1.5 Relationship to Other Projects and the Organisations´s Strategy

Wetterstation 001	RELATIONSHIP TO OTHER PROJECTS		
Programs/ Projects/	**Relationship** (potential/conflict)	**Sanctions**	**Who / when** **WBS Code**
Indoor-Wetterstation	Conflict	Competition	Paul Gnadlinger; Nicolas Goiginger
Smarter Blumentopf	Potential	Support with Know-how	Paul Auer
Smart-Wand	Potential	Support with Know-how	Thomas Toferer

Wetterstation 001	CONNECTION TO THE ORGANISATION´S STRATEGY
Strategy	**Description of connection/relationship**
-	-

1.6 Project Organisation Chart

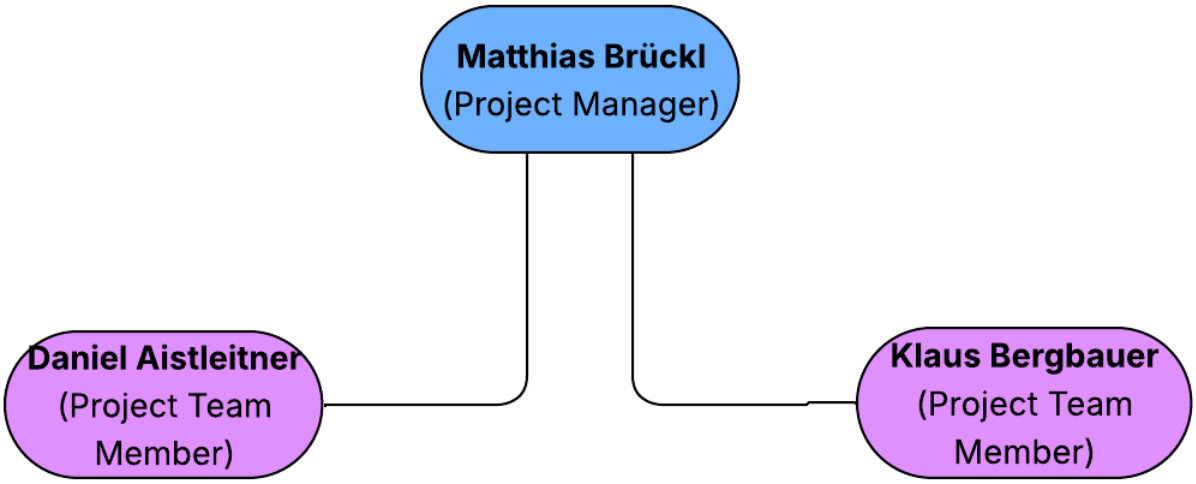

Wetterstation 001	PROJECT-ORGANISATION	
Role in Project	**Field of duties/Skills**	**Name**
Project owner	Financial providence	HTL Wels
Project manager	Backend development	Matthias Brückl
Project team members	1. Frontend development 2. Hardware and 3d Modelling	1. Daniel Aistleitner 2. Klaus Bergbauer
Project members		

1.7 Plan of Objects of Consideration of the Project

Wetterstation 001

PLAN OF OBJECTS OF CONSIDERATION

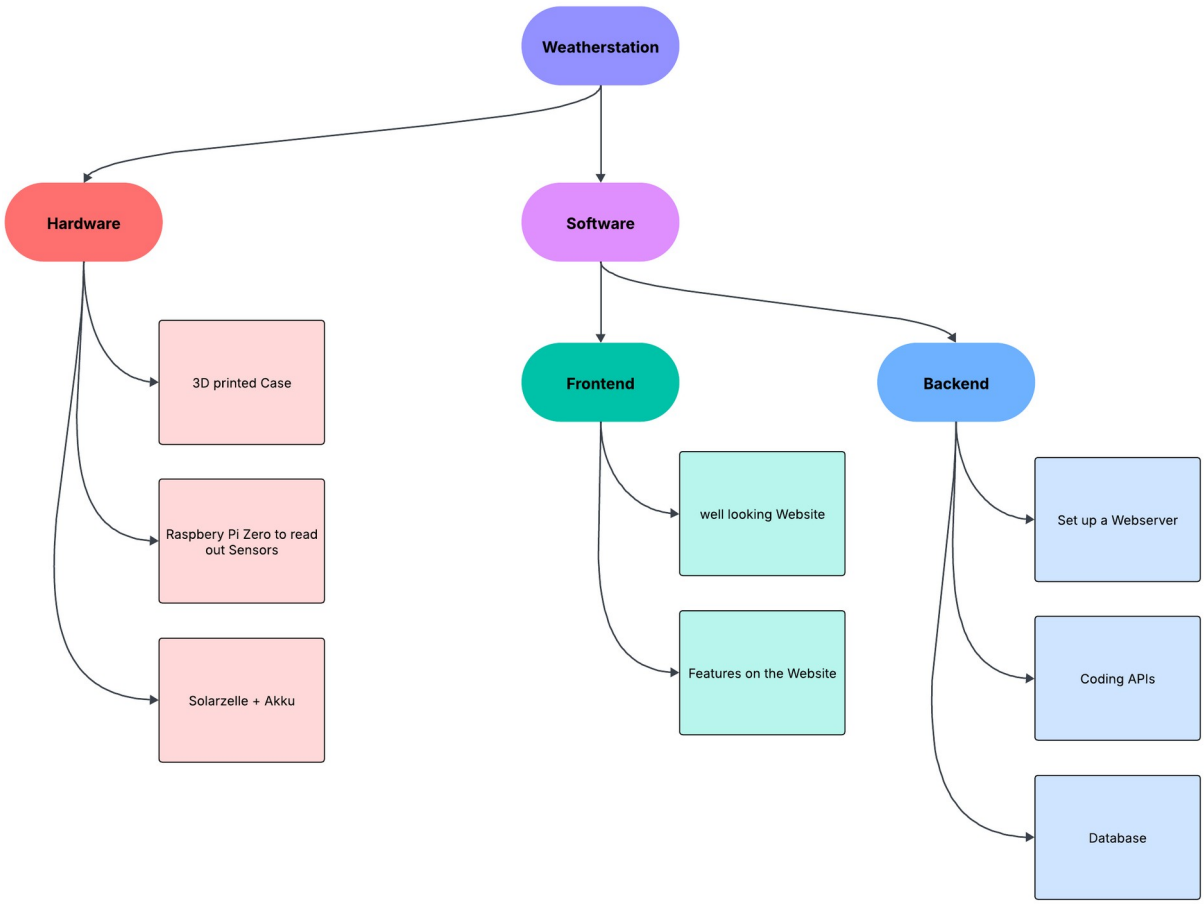

1.8 Work Breakdown Structure (WBS)

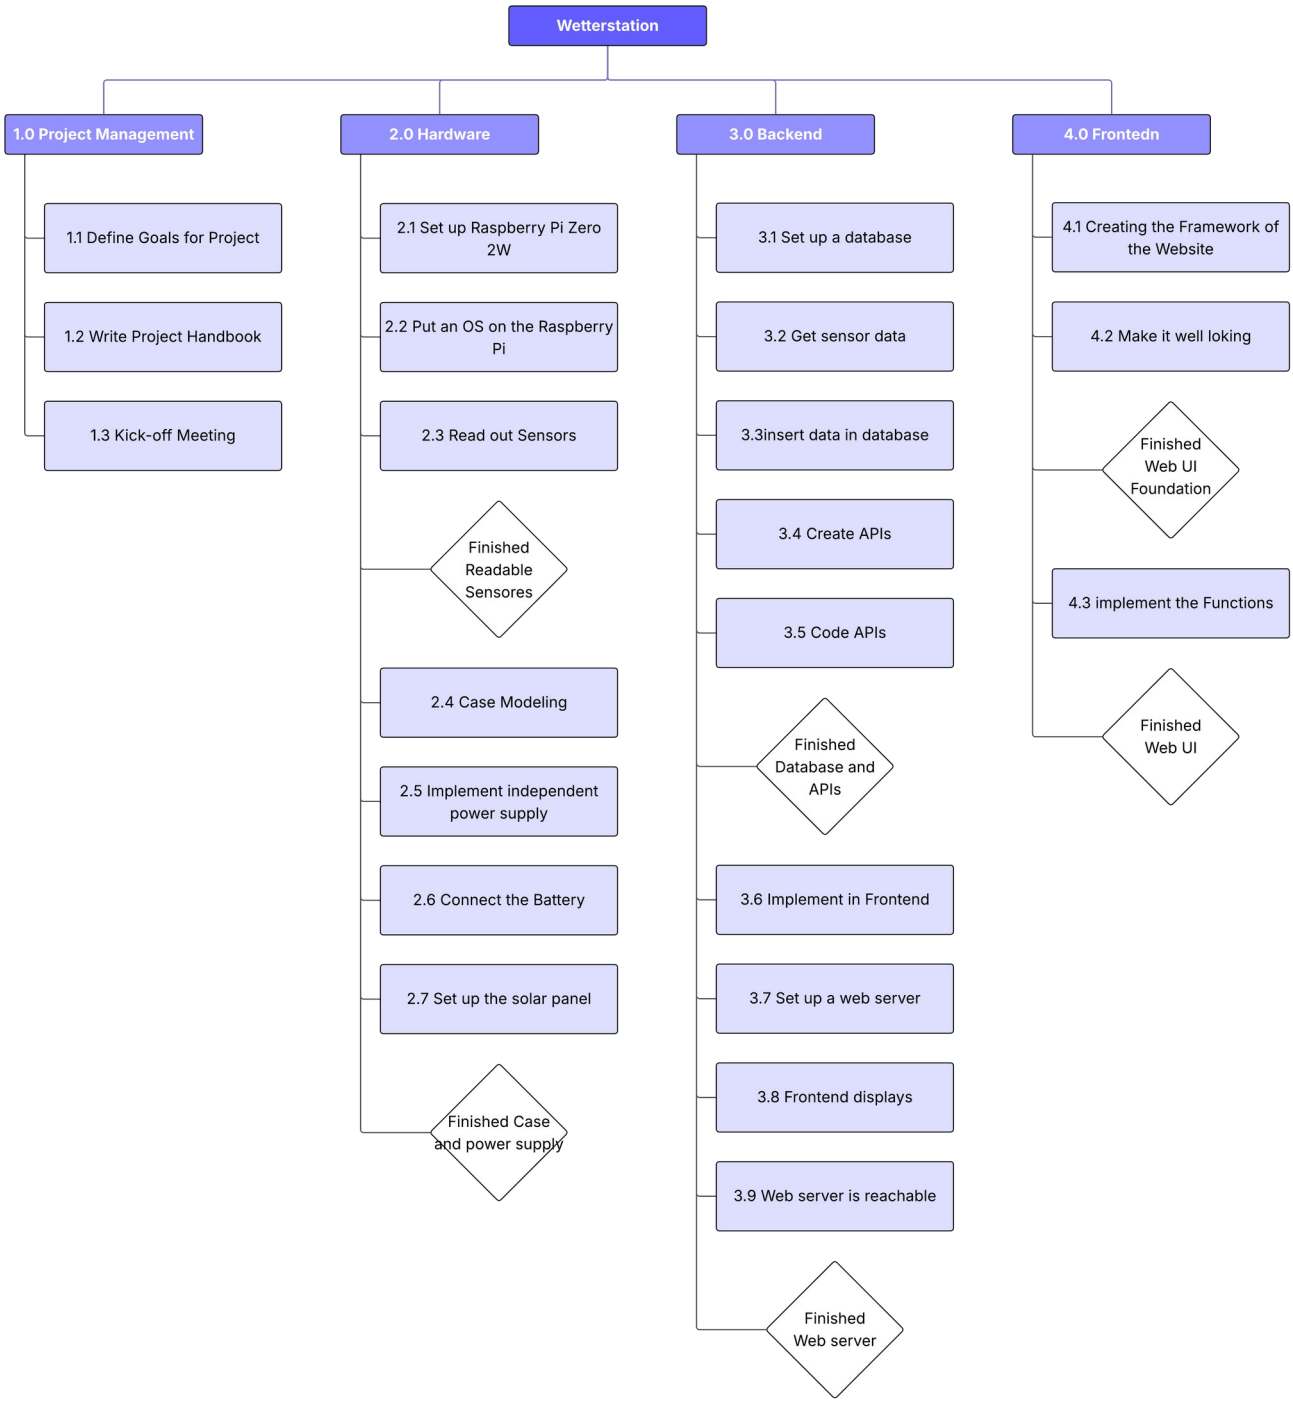

1.9 Project Work-Package Specification

Wetterstation 001	PROJECT WORK-PACKAGE SPECIFICATION
1.1 Setup a Folder Structure	**WP Content** *(What shall be done?)* • Think about a clear folder structure
	WP Result *(What is achieved after WP was finished?)* • Have a clear folder structure
	Progress Measurement *(How is progress measured?)* • Every File has his right place
1.2 Workout Project Requirements	**WP Content** *(What shall be done?)* • Think about the Project Requirements
	WP Result *(What is achieved after WP was finished?)* • Have a clear vision of the Project
	Progress Measurement *(How is progress measured?)* • The Requirements willincrease
1.3 Workout Project Handbook section 1-3	**WP Content** *(What shall be done?)* • Filling the Project-Handbook
	WP Result *(What is achieved after WP was finished?)* • The sections 1-3 have the right entries
	Progress Measurement *(How is progress measured?)* • The Project-Handbook are filling
1.4 Workout Project Handbook section 4-5	**WP Content** *(What shall be done?)* • Filling the Project-Handbook section 4-5
	WP Result *(What is achieved after WP was finished?)* • The sections 4-5 have the right entries
	Progress Measurement *(How is progress measured?)* • The Project-Handbook are filling
1.5 Workout Project Specification Section	**WP Content** *(What shall be done?)* • Filling the Project Specification
	WP Result *(What is achieved after WP was finished?)* • Have a clear Project Specification, which has the right entries
	Progress Measurement *(How is progress measured?)* • The Project Specification are filling

2.1 Raspberry activation	**WP Content** *(What shall be done?)* • Setting up the raspberry
	WP Result *(What is achieved after WP was finished?)* • Make the raspberry useable
	Progress Measurement *(How is progress measured?)* • If raspberry is ready
2.2 Sensor implementation	**WP Content** *(What shall be done?)* • Sensor implementing
	WP Result *(What is achieved after WP was finished?)* • Make the raspberry useable for the sensors
	Progress Measurement *(How is progress measured?)* • If raspberry is ready
2.3 Write Sensor Scripts	**WP Content** *(What shall be done?)* • Make the data from the sensors usable
	WP Result *(What is achieved after WP was finished?)* • The data is displayed in the terminal
	Progress Measurement *(How is progress measured?)* • Scripts are finished for each sensors
2.4 Case modeling	**WP Content** *(What shall be done?)* • Modeling the case of the weather station
	WP Result *(What is achieved after WP was finished?)* • Have a file to print
	Progress Measurement *(How is progress measured?)* • Having a promising model
2.5 Print Case	**WP Content** *(What shall be done?)* • Print the Case
	WP Result *(What is achieved after WP was finished?)* • Having a ready to use case for the weather station • Combination with raspberry and other components
	Progress Measurement *(How is progress measured?)* • Having a successful print • Making the other components fit
2.6 Think about an Energy independent power supply	**WP Content** *(What shall be done?)* • Think about an energy independent power supply
	WP Result *(What is achieved after WP was finished?)* • Have an energy independent concept
	Progress Measurement *(How is progress measured?)* • The concept can be implemented
2.7 Implement the	**WP Content** *(What shall be done?)*

Energy independent power supply	• Installing the independent power supply
	WP Result *(What is achieved after WP was finished?)* • The Weatherstation is powered by solar energy.
	Progress Measurement *(How is progress measured?)* • The Weatherstation is running 24/7
3.1. Basic Framework	**WP Content** *(What shall be done?)* • Programming the Basic Framework of the Frontend
	WP Result *(What is achieved after WP was finished?)* • Creating a functional running program
	Progress Measurement *(How is progress measured?)* • If there are no errors • Program is running
3.2. Website with not yet functional features	**WP Content** *(What shall be done?)* • Programming the website with the necessary features
	WP Result *(What is achieved after WP was finished?)* • Having a not yet functional website
	Progress Measurement *(How is progress measured?)* • Control and looking at the website
3.3. Functionalities	**WP Content** *(What shall be done?)* • Programming the functionalities
	WP Result *(What is achieved after WP was finished?)* • Sensor-data and printing it out
	Progress Measurement *(How is progress measured?)* • If you can see the data on the website
3.4. Design	**WP Content** *(What shall be done?)* • Design of the website **Promotion cum laude zum Dr. med. dent. an der Semmelweis Universität Budapest**
	WP Result *(What is achieved after WP was finished?)* • Having a well looking website
	Progress Measurement *(How is progress measured?)* • Adding simple elements
4.1. Database	**WP Content** *(What shall be done?)*

	• Setup a small database to save
	WP Result *(What is achieved after WP was finished?)* • Having a well modeld Database
	Progress Measurement *(How is progress measured?)* • Values can be stored effectively
4.2. APIs	**WP Content** *(What shall be done?)* • Coding APIs
	WP Result *(What is achieved after WP was finished?)* • Frontend can reach Data
	Progress Measurement *(How is progress measured?)* • Values are displayed on the Frontend
4.3. Web Server	**WP Content** *(What shall be done?)* • Setting up a web server
	WP Result *(What is achieved after WP was finished?)* • A web server is running
	Progress Measurement *(How is progress measured?)* • The website that displays the data can be accessed

1.10 Project Responsibility Matrix

Wetterstation 001

PROJECT-RESPONSIBILITY-MATRIX

WBS-Code	WP-Title / Roles & Environment	External project owner	Project owner	Project manager	Project assistant	Project team member 1	Project team member 2	Project team member 3	Project team member 4	Project team member 5	Project member 1	Project member 2	Project member 3	Project coach
1.0	**Project Management**		**I**	**R**		**C**	**C**							
1.0.1	Define goals for Project		I	R		C	C							
1.0.2	Write Project-Handbook		I	R		C	C							
1.0.3	Kick-off meeting		I	R		C	C							
1.1	**Hardware**		**I**	**C**		**I**	**R**							
1.1.1	Set up the Raspberry Pi Zero 2W		I	I		I	R							
1.1.1.1	Put an OS on the Raspberry Pi Zero		I	I		I	R							
1.1.1.2	Use correct resistors and sensors		I	I		I	R							
1.1.1.3	Read out sensors		I	C		I	R							
1.1.2	Case modeling		I	I		I	R							
1.1.3	Implement independent power supply		I	I		I	R							
1.1.3.1	Connect the battery		I	I		I	R							
1.1.3.2	Setting up the Solar panel		I	I		I	R							
1.2	**Backend**		**I**	**R**		**C**	**C**							
1.2.1	Set up a database		I	R		I	C							
1.2.1.1	Get Sensor Data		I	R		I	C							
1.2.1.2	Insert in data in database		I	R		I	C							
1.2.2	Create APIs		I	R		C	I							
1.2.2.1	Code APIs		I	R		I	I							
1.2.2.2	Implement in Frontend		I	C		R	I							
1.2.3	Set up a web server		I	R		C	I							
1.2.3.1	Frontend displays		I	R		C	I							
1.2.3.2	Web server is reachable		I	R		I	I							
1.3	**Frontend**		**I**	**I**		**R**	**I**							
1.3.1	Creating the Framework of the website		I	I		R	I							

1.3.2	Make it well looking		I	I		R	I							
1.3.3	Implement the functions		I	C		R	I							

Functions
R .....Responsible
C .....Contribution
I .....has to be informed

1.11 Milestoneplan

Wetterstation 001	MILESTONEPLAN			
WBS-Code	**Milestone**	**Plan date**	**Revised date**	**Actual date**
4	Finished readable sensors	12.02.2026		
7	Finished case and power supply	30.03.2026		
10	Finished Web UI Foundation	17.03.2026		
16	Finished Database and APIs	26.03.2026		
13	Finished Fronted	29.04.2026		
18	Finished Web Server	15.05.2026		
20	Finished Project	10.06.2026		

*In order of plan dates.

1.12 Project Bar Chart

		Name	Dauer	Start	Ende	Vorgänger	Ressourcen
1		Software installation	2 tage?	12.01.26, 08:00	13.01.26, 17:00		Laptop
2		Raspberry activation	12 tage?	12.01.26, 08:00	27.01.26, 17:00		Laptop;Raspberry Pi Imager;Raspberry...
3		Sensor implementation	4 tage?	28.01.26, 08:00	02.02.26, 17:00	2	BME280;DHT22;Raspberry Pi Zero 2W
4		Finished readble sensors	0 tage?	02.02.26, 17:00	02.02.26, 17:00	3	
5		Work out energy independent power supp	15 tage?	03.02.26, 08:00	23.02.26, 17:00	4	Raspberry Pi Zero 2W;Battery;Solar Pa...
6		Case Modeling	15 tage?	05.03.26, 08:00	25.03.26, 17:00	5	Laptop;3D-Printer;ABS-Filament;Onesh...
7		Finished Case and power supply	0 tage?	30.03.26, 07:00	30.03.26, 08:00	6	
8		Framework for Web UI	10 tage?	11.02.26, 08:00	24.02.26, 17:00		Laptop;Visual Studio Code
9		Web UI with not yet functional features	15 tage?	25.02.26, 08:00	17.03.26, 17:00	8	Laptop;Visual Studio Code
10		Finished Web UI Foundations	0 tage	17.03.26, 17:00	17.03.26, 17:00	9	
11		Functionalities in Web UI	12 tage?	18.03.26, 08:00	02.04.26, 17:00	9;15	Laptop;Visual Studio Code
12		Design	12 tage?	03.04.26, 08:00	20.04.26, 17:00	11	Laptop;Visual Studio Code
13		Finished Frontend	0 tage	20.04.26, 17:00	20.04.26, 17:00	12	
14		Setup a Database	15 tage?	03.02.26, 08:00	23.02.26, 17:00	4AA	Laptop;Raspberry Pi Zero 2W;DataGrip
15		Creating APIs	15 tage?	24.02.26, 08:00	16.03.26, 17:00	14	Laptop;Raspberry Pi Zero 2W;Visual St...
16		Finished Database&APIs	0 tage	16.03.26, 17:00	16.03.26, 17:00	15	
17		Create Web Server	12 tage?	21.04.26, 08:00	06.05.26, 17:00	13;16	Laptop;Raspberry Pi Zero 2W;Visual St...
18		Finished Web Server	0 tage	06.05.26, 17:00	06.05.26, 17:00	17	
19		setup mDNS	12 tage	07.05.26, 08:00	22.05.26, 17:00	18	Laptop;Raspberry Pi Zero 2W;Visual St...
20		Finished Project	0 tage	10.06.26, 07:00	10.06.26, 08:00	7;19	

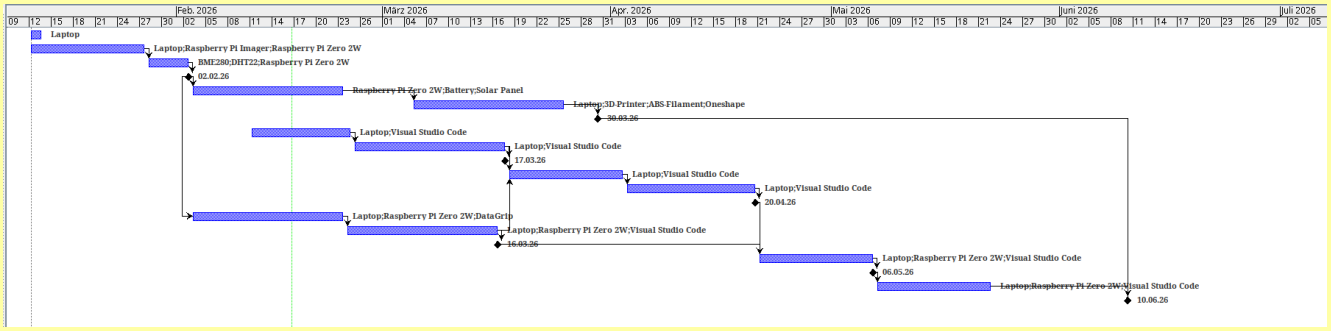

1.13 Resource Plan

Wetterstation 001	Resource Plan					
WBS-Code	**Phase/Work-package**	**Type of resource**	**Planned quantity (days)**	**Revised quantity (days)**	**Actual quantity (days)**	**Deviation (days)**
2	Raspberry activation	Raspberry Pi Zero 2W, Laptop, Raspberry Pi Imager	12	12	12	0
3	Sensor implementation	Raspberry Pi Zero 2W, DHT22, BME280	12			
5	Work out energy independent power supply	Raspberry Pi Zero 2W, Battery, solar panel	15			
6	Case modeling and printing	3D-Printer, ABS-Filament, Laptop, Oneshape	15			
8	Framework fro Web UI	Laptop, Virtual Studio Code	10			
9	Web UI with not yet functional features	Laptop, Virtual Studio Code	15			
11	Functionalities in Web UI	Laptop, Virtual Studio Code	12			
12	Web UI Design	Laptop, Virtual Studio Code	12			
14	Setup a Database	Laptop, Raspberry Pi Zero 2W, DataGrip	15			
15	Creating APIs	Laptop, Raspberry Pi Zero 2W, Virtual Studio Code	15			
17	Create Web Server	Laptop, Raspberry Pi Zero 2W, Virtual Studio Code	12			
19	Setup mDNS	Laptop, Raspberry Pi Zero 2W, Virtual Studio Code	12			

1.14 Project Cost Plan

Wetterstation 001	PROJECT COST PLAN				
WBS-Code, WP-Title	Type of Cost	Planned cost	Revised cost	Actual cost	Deviation
1. Hardware	• Personnel	0€			
	• Material	98€			
	• External services	0€			
	• Other	0€			
	Total	98€			
2. Software	• Personnel	0€			
	• Material	0€			
	• External services	0€			
	• Other	0€			
	Total	0€			
3. Frontend	• Personnel	0€			
	• Material	0€			
	• External services	0€			
	• Other	0€			
	Total	0€			
Project cost		98€			

1.15 Project Communication

Wetterstation 001	PROJECT-COMMUNICATION			
Title	**Objectives, Content**	**Participants**	**Schedule**	**Location**
Project owner meeting	• project status • decisions • acceptance of progress report	Project owner, Project manager	Not yet scheduled	Teacher Table
Project controlling meeting	• project status • controlling of tasks, schedule, resources, costs • controlling of project environments • social controlling • prepare proposal for decision	Project manager, Project team, Project coach	Every Monday at 11 o clock	Last Row, classroom T233
Subteam meeting	• Coordination of subteams • Discussion of problems	Subteam	Every Monday at 11 o clock	Last Row, classroom T233
	•			

1.16 Project „Rules“

Communication:

- **Weekly Meetings:** The participation of the Project Team Member and the Project Manager in the Weekly Meetings is very important. The meeting is scheduled every Monday at 11 o clock.
- **File sharing:** All files belonging to the project must be published in the GitHub repository. No other ways to share files are allowed.
- **Communication channels:** All important information will be published in the team group.

General Collaboration:

- **Time Management:** Each team member is responsible for their own work packages. These must be completed by the deadline. If more time is needed, this must be requested promptly.
- **Support:**
  - If help is needed with a work package, it must be requested promptly.
  - If someone needs help and you have the time and are able to help, you are obligated to do so.

Documentation:

- **Version Control:** The Project Handbook must be updated regularly. Significant changes require a new version number and an entry in the document history.

Technical Standard:

- **Hardware Care:** Care must be taken with the hardware components, and they must not be damaged or broken in any way. If this happens, the affected part must be replaced.

1.17 Project Risk Analysis

		PROJECT RISK ANALYSIS							
WBS-Code	WBS-description	Risk-description	Priority	Benefit /Cost	Probability	Risk-value	Delay	Avoiding action	Cost for minimizing risk
(Code)	*(Text)*	*(Text)*	*(Range)*	*(iuro)*	*(Percentage)*	*(iuro)*	*(iWeeks)*	*(Text)*	*(Euro)*
2	Raspberry activation	break	1	30€	10%	30€	1-2Weeks	Take Care	0€
3	Senor implementation	Sensor breaks	1	5-10€	10%	5-10€	1-2Weeks	Take Care	0€
5	Workout energy independent supply	Provide not enough electricity	2	20€	20%	20€	1-2Weeks	First Think, than buy	15€
6	Case Modeling	Wrong size	4	5€	40%	5€	½ Week	Measure correctly	0€
14	Setup a Database	Database is too small	2	0€	10%	0€	½ Week	Think first about the right size	0€
15	Creating APIs	APIs don't share the data	5	0€	15%	0€	½ Week	Have a clear structure	0€
17	Create Web Server	The server don't start	3	0€	10%	0€	½ Week	Inform you how to create a server	0€
18	setup mDNS	DNS doesn't work	3	0€	20%	0€	½ Week		0€
Project total				60€		60€	5½ Weeks		15€

1.18 Project Documentation

Area	Description
File	In the GitHub Repository: Directory named “Documentation”
Access Authorization	Everyone from the Project Team has access to the documentation
Naming convention	DDMMYYYY_version_name.docx
Rules	

2 Project Start

2.1 Minutes– Project Start

2.1.1 Project Start Workshop

2.1.2 Follow-up Workshop

2.1.3 Project Owner Meeting

3 Project Co-ordination

3.1 Approval of Work-packages

Wetterstation 001	APPROVAL OF WORK-PACKAGES				
WBS-Code	**Work-package**	**WP-Owner**	**Date**	**Approval by**	**Signature**
2	Raspberry activation	Berbauer K.	27.01.26		
3	Sensor implementation	Berbauer K.	02.02,26		
5	Work out energy independent power supply	Berbauer K.			
6	Case Modeling	Berbauer K.			
8	Framework for Web UI	Aistleitner D.			
9	Web UI with not yet functional features	Aistleitner D.			
11	Functionalities in Web UI	Aistleitner D.			
12	Design	Aistleitner D.			
14	Setup a Database	Brückl M.			
15	Creating APIs	Brückl M.			
17	Create Web Server	Brückl M.			
19	setup mDNS	Brückl M.			

3.2 Minutes – Project Co-ordination

4 Project Controlling

4.1 Project Status Report

Wetterstation 001	PROJECT STATUS REPORT as of .....
 Project crisis Project in difficulties Project according to plan ✓	**1) Overall Status:** • **The project is progressing well. Raspberry Pi Zero 2W has been successfully set up with SSH and Wi-Fi enabled. DHT11 sensor testing is underway, and the basic React website structure is complete.**

2) Status Project objectives • **Set up Raspberry Pi Zero 2W with OS Lite** • **Enable remote access via SSH** • **Test DHT11 temperature/humidity sensor** • **Develop React-based web interface**	**Activities:** • **Raspberry Pi successfully configured** • **DHT11 sensor integrated and tested (command line output working)** • **Basic website structure implemented in React**
3) Status Project progress • **Hardware setup: 80% complete (waiting for hardware shipment)** • **Sensor integration: 55% complete (testing phase)** • **Website development: 20% complete (structure** • **done, output pending)**	**Activities:** • **Raspberry OS Lite installed on 32GB Micro SD card** • **SSH and Wi-Fi connectivity established** • **DHT11 sensor displaying data in terminal** • **React frontend Framework implemented**
4) Status Schedule • **On track - all milestones met by 03.02.2026** • **No delays reported**	**Activities:** • **Phase 1 (Hardware Setup) completed on time (with lend Raspberry)** • **WBS 3 (Sensor Testing) in progress as planned**
5) Status Resources/costs • **Raspberry Pi Zero 2W (lended)** • **32GB Micro SD card** • **DHT11 sensor (for testing)** • **DHT22 sensor** • **BMP280**	**Activities:** • **Nearly all required hardware procured** • **Budget within limits** • **No additional resource requirements** • **identified**
6) Status Context • **Raspberry Pi Imager used for OS installation** • **PowerShell used for remote SSH connection**	**Activities:** • **Documentation of setup procedure completed** • **Network connectivity stable** • **No external blockers or dependencies**

7) Status Organisation/culture • **Author: Klaus Bergbauer** • **Collaboration ongoing**	**Activities:** • **Knowledge sharing via progress documentation** • **Testing and development workflow established** • **Communication channels functional (SSH, Wi-Fi)**

4.2 Project Status Report

Wetterstation 001	PROJECT STATUS REPORT as of	



2) Overall Status:
- **The project is progressing well. Raspberry Pi Zero 2W can readout the DHT22 and the BME280 sensors. The first steps towards a database have been taken and the Web User Interface has been optimized.**

2) Status Project objectives • **Integrate high-precision sensors (DHT22, BME280)** • **Automate data retrieval via scripting** • **Improve React frontend design**	**Activities:** • **DHT22 & BME280 successfully wired and recognized** • **Custom script for data reading completed** • **UI styling and layout optimization finished**
3) Status Project progress • **Hardware setup: 100% (All sensors arrived and installed)** • **Data Processing: 90% (Scripts functional)** • **Website development: 40% (UI refined)**	**Activities:** • **Replaced DHT11 with superior DHT22/BME280 sensors** • **Developed and debugged data collection script** • **Implemented CSS/styling updates to the React WebUI**
4) Status Schedule • **On track - all milestones met by 16.02.2026** • **No delays reported**	**Activities:** • **WP 2 (Raspberry activation) completed on time (with lend Raspberry)** • **WP 3 (Sensor implementation) completed**
5) Status Resources/costs • **Raspberry Pi Zero 2W (lended)** • **32GB Micro SD card** • **DHT22 sensor** • **BME280**	**Activities:** • **Nearly all required hardware procured** • **Budget within limits** • **No additional resource requirements identified**

6) Status Context • **PowerShell used for remote SSH connection** • **Python Scripts used to read out the sensors** • **data output verified via terminal**	**Activities:** • **Documented the pinout configuration for the new sensors** • **No external blockers or dependencies**
7) Status Organisation/culture • **Author: Matthias Brückl** • **Collaboration ongoing** • **Documentation updated for new hardware**	**Activities:** • **Knowledge sharing via progress documentation** • **Testing and development workflow established** • **new Scripts are published to the other Projektmembers**

4.3 Additional Project Status Reports

4.4 Minutes – Project controlling

4.4.1 Project Controlling Meetings

4.4.2 Project Owner Meetings

5 Project Close Down

5.1 Project Close Down Report

Wetterstation 001	PROJECT CLOSE DOWN REPORT

1) Overall impression	**2) Reflection: Fulfilment of objectives**
3) Reflection: Deliverables / Schedule	
4) Reflection: Resources / Costs	
5) Reflection: Internal Organisation / Environmental Relationships	
6) Performance appraisal (Project owner, Project manager, Project member)	**7) Lessons learned (Summary of Experiences and suggestions for improvement)**

8) Post-Project Phase Planning, Additional Tasks

To-Do	Owner	Schedule

9) Project Close Down

....

<Name> (Project owner) *<Name>* (Project manager)

5.2 Minutes – Project Close Down

5.2.1 Project Close Down Workshop
